


Appendix 2L

INITIAL PROJECT SCHEDULE

KELOWNA GENERAL HOSPITAL P3 - ACC PROJECT

Preliminary - Thu 8/7/08

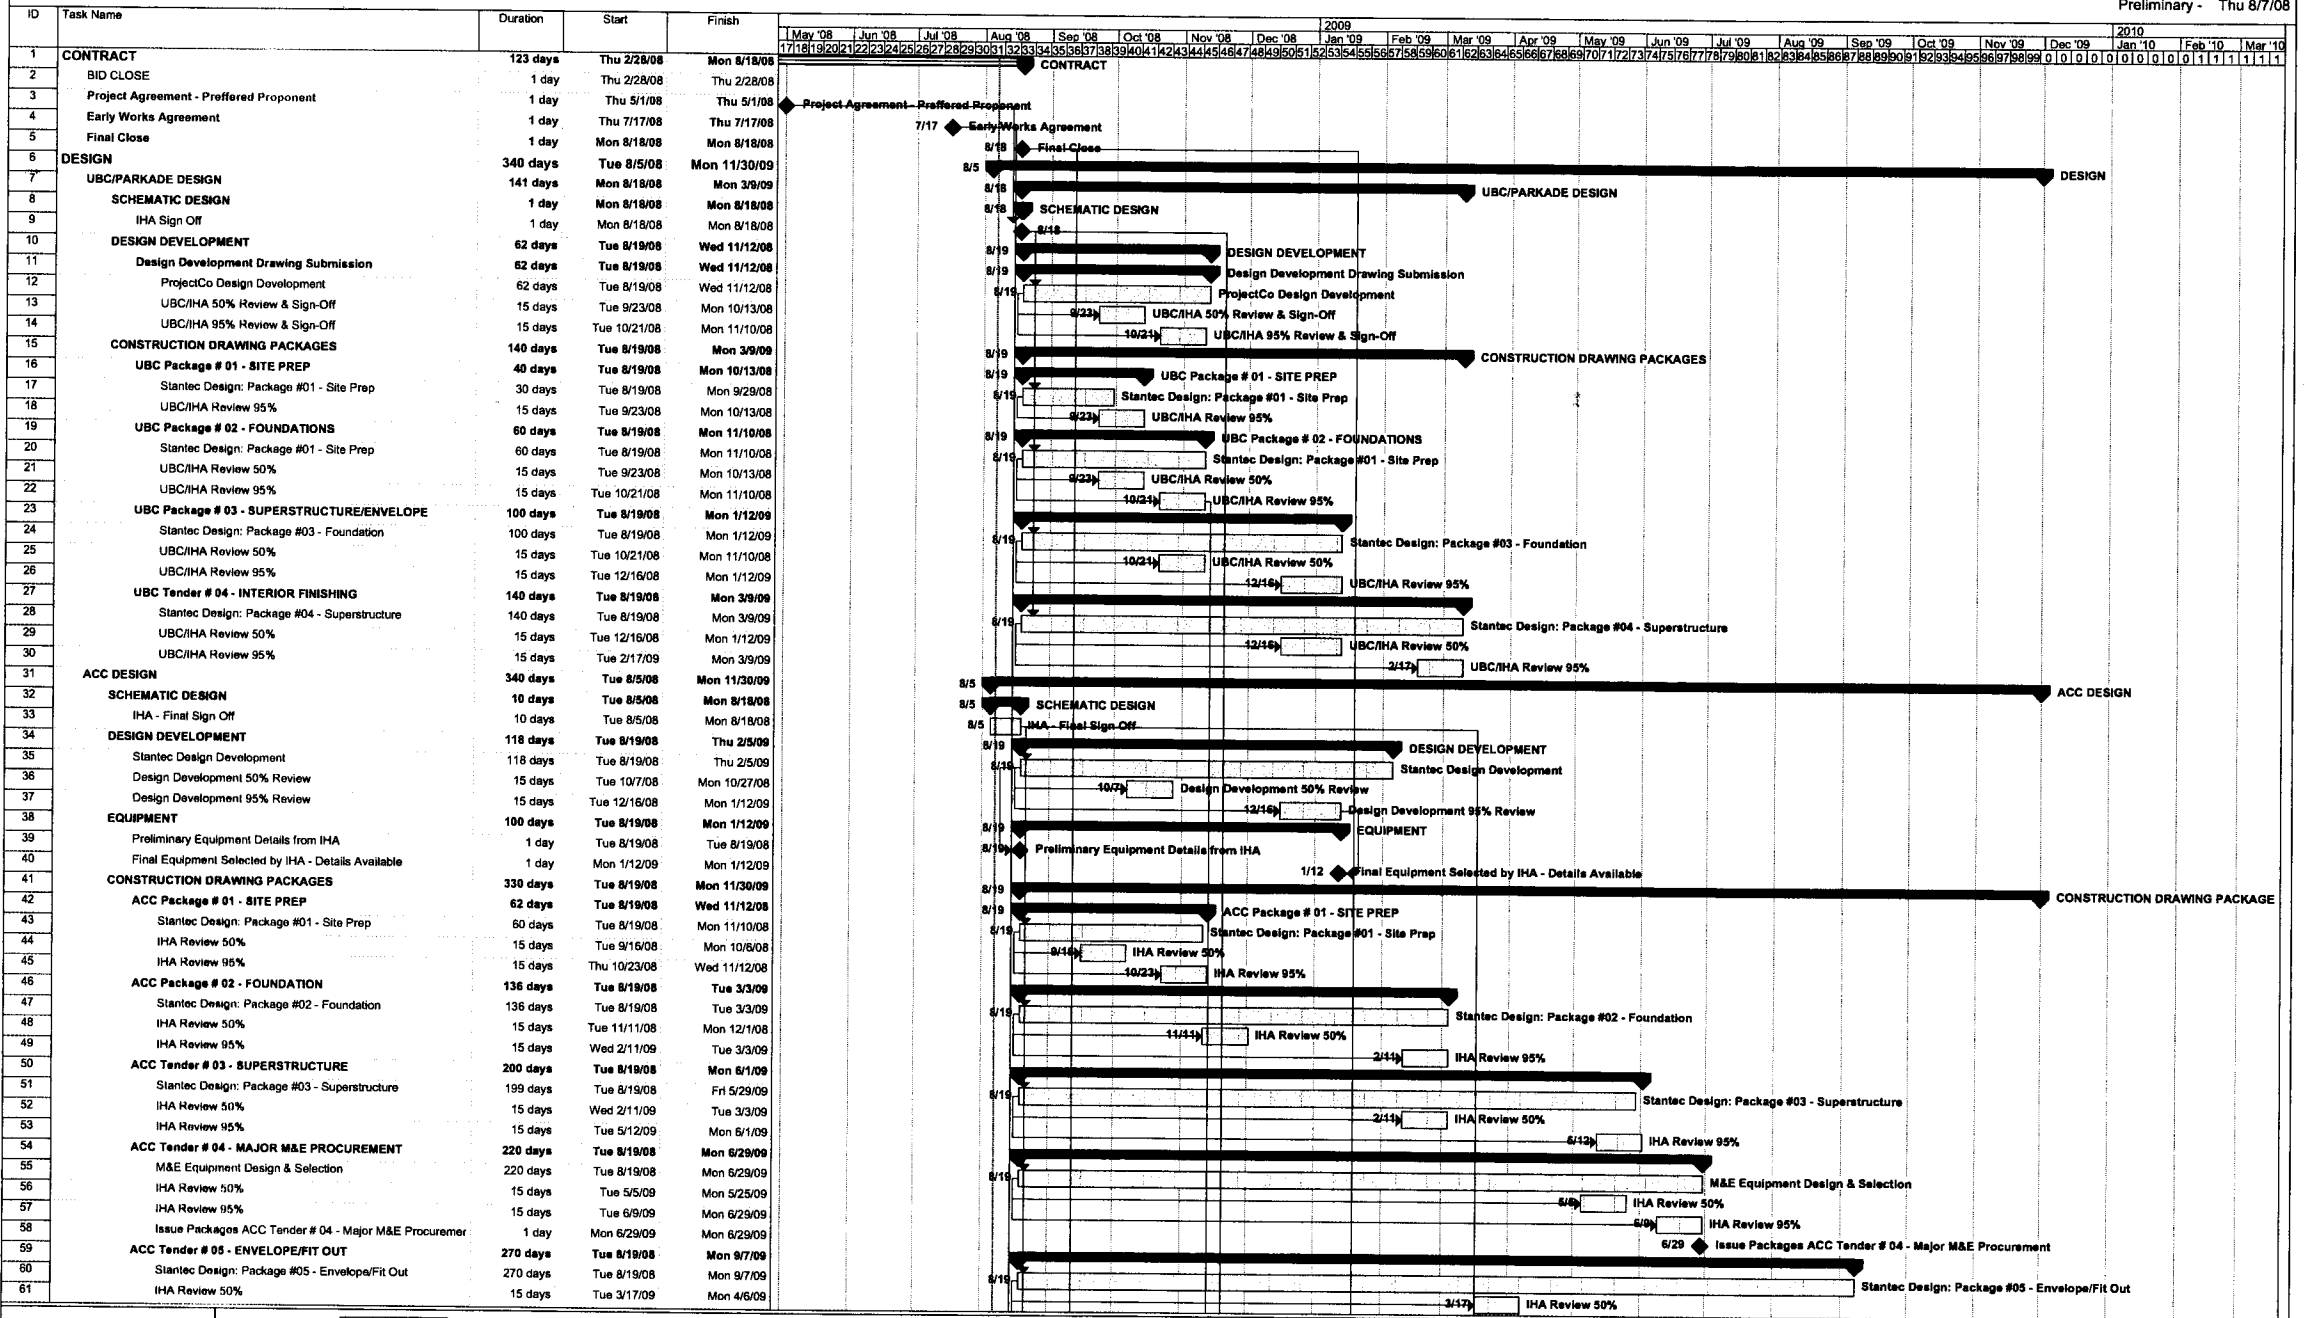


Project: VGH - Summary Schedule 2 Date: Thu 8/7/08

Task Split Progress Milestone Summary Project Summary External Tasks External Milestone Deadline

KELOWNA GENERAL HOSPITAL P3 - ACC PROJECT

Preliminary - Thu 8/7/08

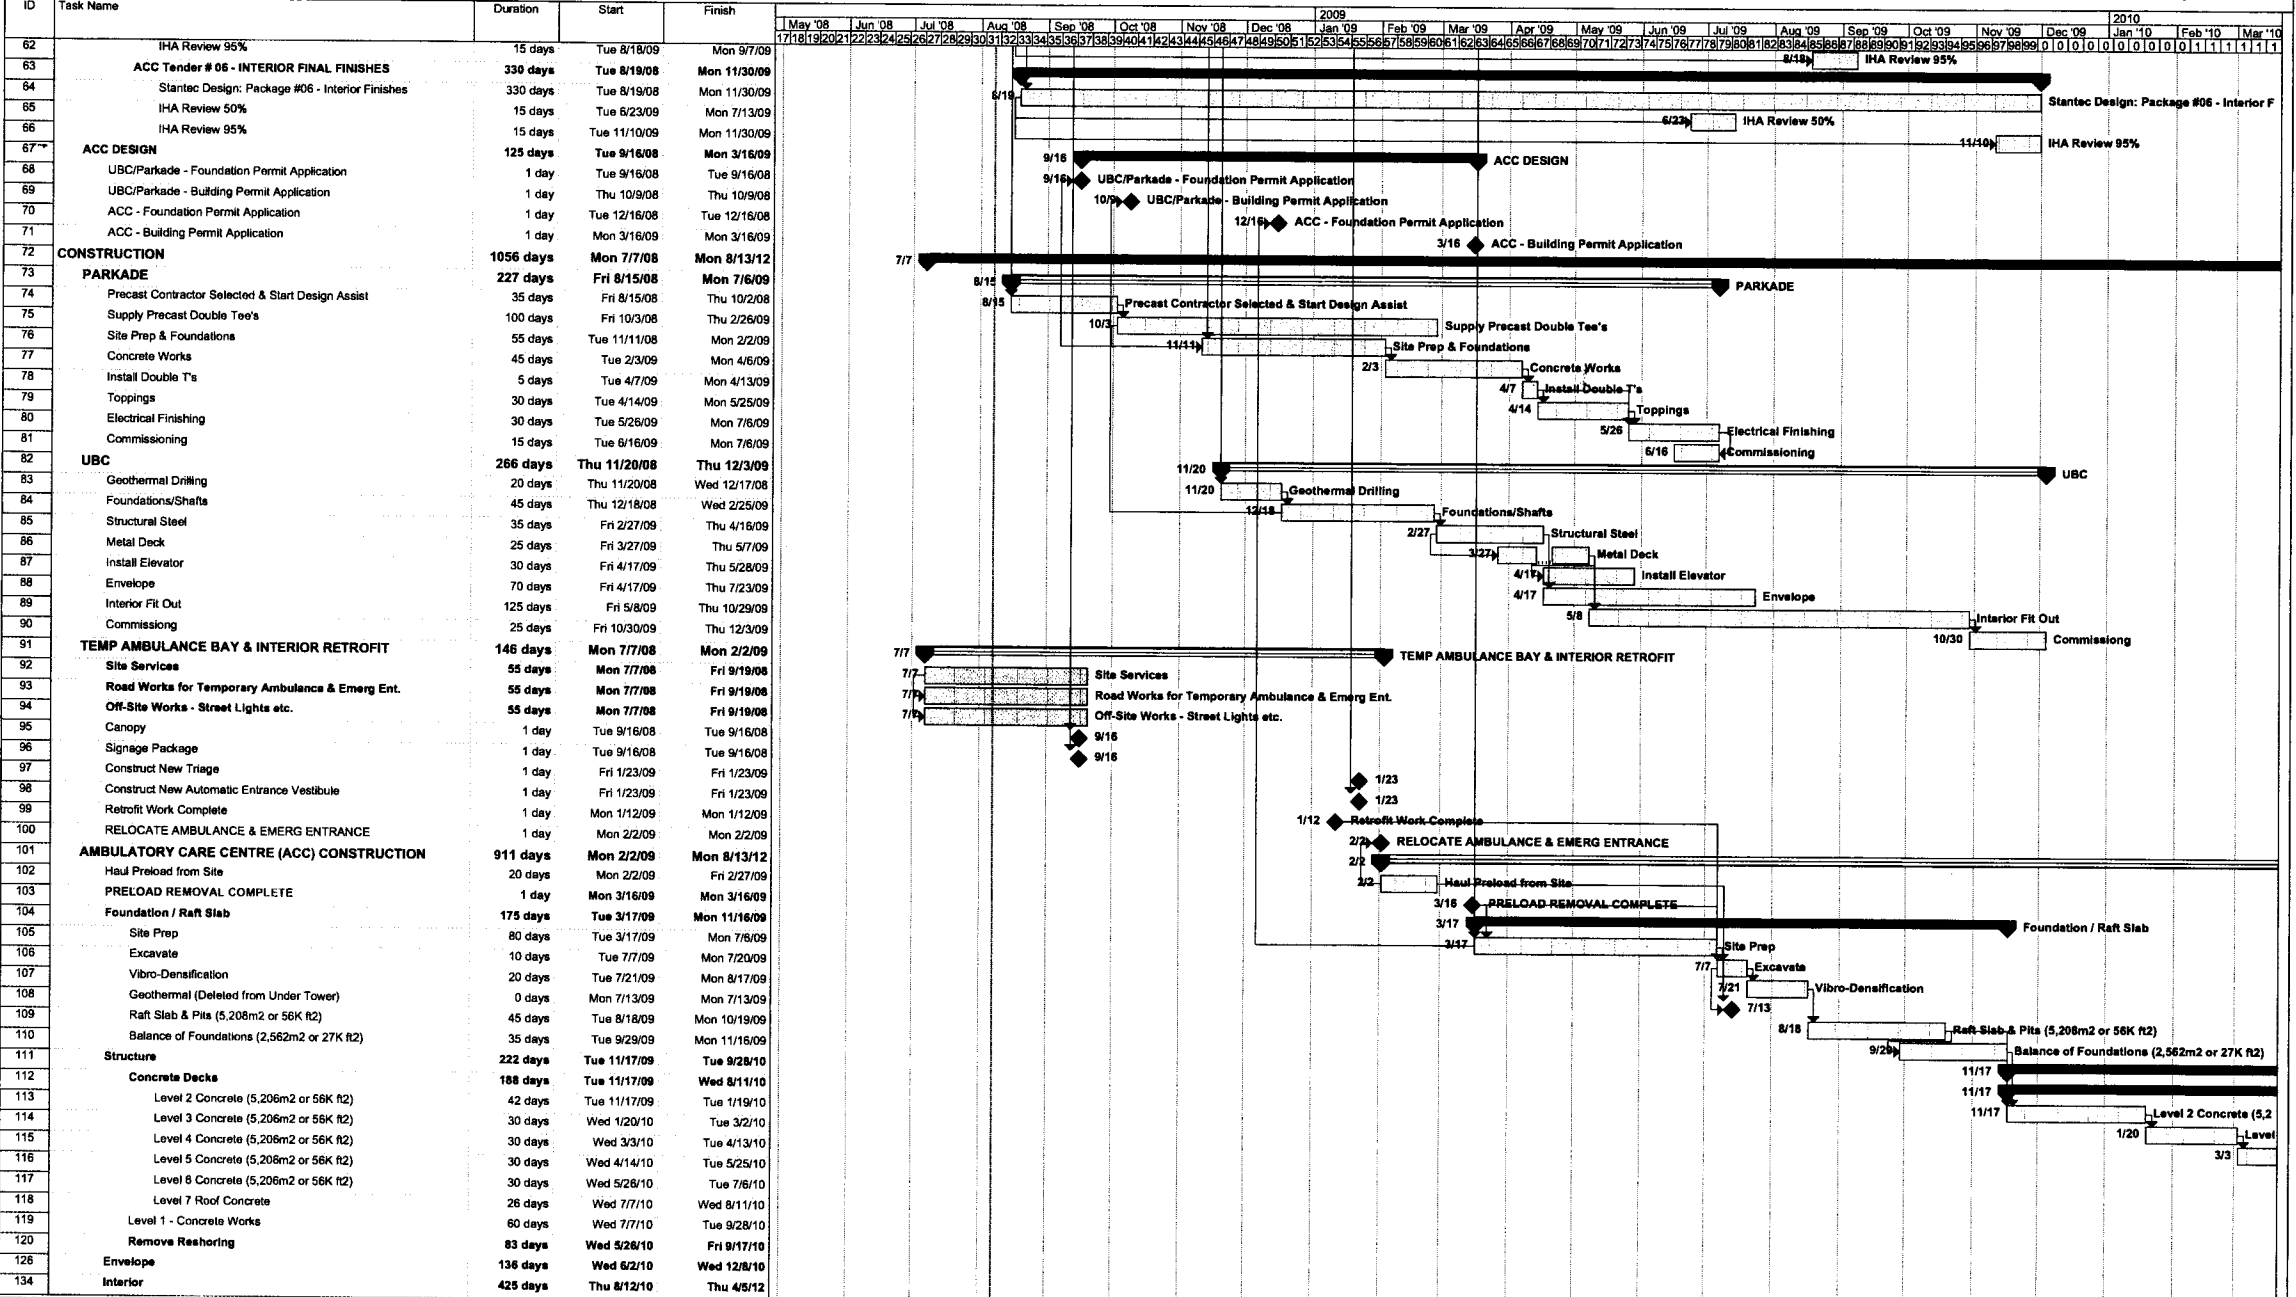

Project: VGH - Summary Schedule 2
Date: Thu 8/7/08

Task Progress Summary External Tasks Deadline

Split Milestone Project Summary External Milestone

VERNON JUBILEE HOSPITAL - DIAGNOSTIC AND TREATMENT BUILDING

Preliminary Schedule v.8 (with added floors) - Fri 8/8/08

ID	Task Name	Duration	Start	Finish	2008												2009												2010												2011											
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec
1	CONTRACT	123 days	Thu 2/28/08	Mon 8/18/08																																																
2	BID CLOSE	1 day	Thu 2/28/08	Thu 2/28/08																																																
3	Project Agreement - Preferred Proponent	1 day	Thu 5/1/08	Thu 5/1/08																																																
4	Early Works Agreement in Place	1 day	Thu 7/17/08	Thu 7/17/08																																																
5	Final Close	1 day	Mon 8/18/08	Mon 8/18/08																																																
6	EARLY WORKS	129 days	Fri 7/18/08	Wed 12/1/09																																																
7	Commence site enabling design work	1 day	Fri 7/18/08	Fri 7/18/08																																																
8	Geotechnical Investigation and Report	15 days	Fri 7/18/08	Thu 8/7/08																																																
9	Site Survey	15 days	Fri 7/18/08	Thu 8/7/08																																																
10	Secure New Hydro Right Of Way - By IH	60 days	Fri 7/18/08	Thu 10/9/08																																																
11	Relocate Primary Electrical Service	60 days	Fri 10/10/08	Thu 1/8/09																																																
12	U/G Service relocations	60 days	Thu 10/23/08	Wed 1/21/09																																																
13	Precondition survey of buildings to be demolished	20 days	Fri 7/18/08	Thu 8/14/08																																																
14	IHA review of hoarding plan	10 days	Mon 8/4/08	Fri 8/15/08																																																
15	Demolition Works - Phase 1	25 days	Tue 10/7/08	Mon 11/10/08																																																
16	Construct Upper Parking Lot	30 days	Tue 11/11/08	Mon 12/29/08																																																
17	Temporary works at Emerg Entry	20 days	Tue 11/25/08	Mon 12/29/08																																																
18	Construct Mockups	30 days	Fri 9/12/08	Thu 10/23/08																																																
19	Mockup Review & Approval	10 days	Fri 10/24/08	Thu 11/6/08																																																
20	Demolition Works - Phase 2	25 days	Tue 11/11/08	Mon 12/15/08																																																
21	DESIGN	315 days	Tue 8/5/08	Thu 10/29/09																																																
22	SCHEMATIC DESIGN	1 day	Mon 8/18/08	Mon 8/18/08																																																
23	IHA Sign Off Req'd	1 day	Mon 8/18/08	Mon 8/18/08																																																
24	DESIGN DEVELOPMENT	95 days	Tue 8/19/08	Mon 1/5/09																																																
25	50% Drawing Submission & Review	50 days	Tue 8/19/08	Mon 10/27/08																																																
26	ProjectCo 50% Design Development	30 days	Tue 8/19/08	Mon 9/29/08																																																
27	Graham Review	5 days	Tue 9/30/08	Mon 10/6/08																																																
28	Black & MacDonald Review	5 days	Tue 10/7/08	Mon 10/13/08																																																
29	IHA Review & Sign-Off	15 days	Tue 10/7/08	Mon 10/27/08																																																
30	95% Drawing Submission & Review	45 days	Tue 10/28/08	Mon 1/5/09																																																
31	ProjectCo 95% Design Development	25 days	Tue 10/28/08	Mon 12/1/08																																																
32	Graham Review	5 days	Tue 12/2/08	Mon 12/8/08																																																
33	Black & MacDonald Review	5 days	Tue 12/9/08	Mon 12/15/08																																																
34	IHA Review & Sign-Off	15 days	Tue 12/9/08	Mon 1/5/09																																																
35	Equipment	50 days	Tue 8/19/08	Mon 10/27/08																																																
36	Preliminary Equipment Details required from IHA	1 day	Tue 8/19/08	Tue 8/19/08																																																
37	Final Equipment Details required from IHA	1 day	Mon 10/27/08	Mon 10/27/08																																																
38	CONSTRUCTION DRAWINGS	315 days	Tue 8/5/08	Thu 10/29/09																																																
39	VJH Tender # 01 - SITE ENABLING	45 days	Tue 8/5/08	Mon 10/6/08																																																
40	Construction Dwg. Submission & Review	30 days	Tue 8/5/08	Mon 9/15/08																																																
41	ProjectCo Const. Dwg. Design	10 days	Tue 8/5/08	Mon 8/18/08																																																
42	Graham Review	5 days	Tue 8/19/08	Mon 8/25/08																																																
43	Black & MacDonald Review	5 days	Tue 8/26/08	Mon 9/1/08																																																
44	IHA Review & Sign-Off	15 days	Tue 8/26/08	Mon 9/15/08																																																
45	Issue Packages ACC Tender # 01 - Site Enabling	5 days	Tue 9/16/08	Mon 9/22/08																																																
46	Trade Submissions	5 days	Tue 9/23/08	Mon 9/29/08																																																
47	Graham Evaluation & Award	5 days	Tue 9/30/08	Mon 10/6/08																																																
48	VJH Tender # 02 - FOUNDATION & CIVIL	140 days	Tue 8/19/08	Mon 3/9/09																																																
49	50% Construction Dwg. Submission & Review	60 days	Tue 8/19/08	Mon 11/10/08																																																
50	ProjectCo 50% Const. Dwg. Design	40 days	Tue 8/19/08	Mon 10/13/08																																																
51	Graham Review	5 days	Tue 10/14/08	Mon 10/20/08																																																
52	Black & MacDonald Review	5 days	Tue 10/21/08	Mon 10/27/08																																																
53	IHA Review & Sign-Off	15 days	Tue 10/21/08	Mon 11/10/08																																																
54	Final Construction Dwg. Submission & Review	60 days	Tue 11/11/08	Mon 2/9/09																																																
55	ProjectCo Const. Dwg. Design	40 days	Tue 11/11/08	Mon 1/12/09																																																

Project: VERNON - Summary Schedul Date: Fri 8/8/08

Task: Progress Milestone

Summary: Rolled Up Task:


Rolled Up Critical Task: Rolled Up Milestone:

Rolled Up Progress: Split:

External Tasks: Project Summary:

Group By Summary: Deadline:

VERNON JUBILEE HOSPITAL - DIAGNOSTIC AND TREATMENT BUILDING

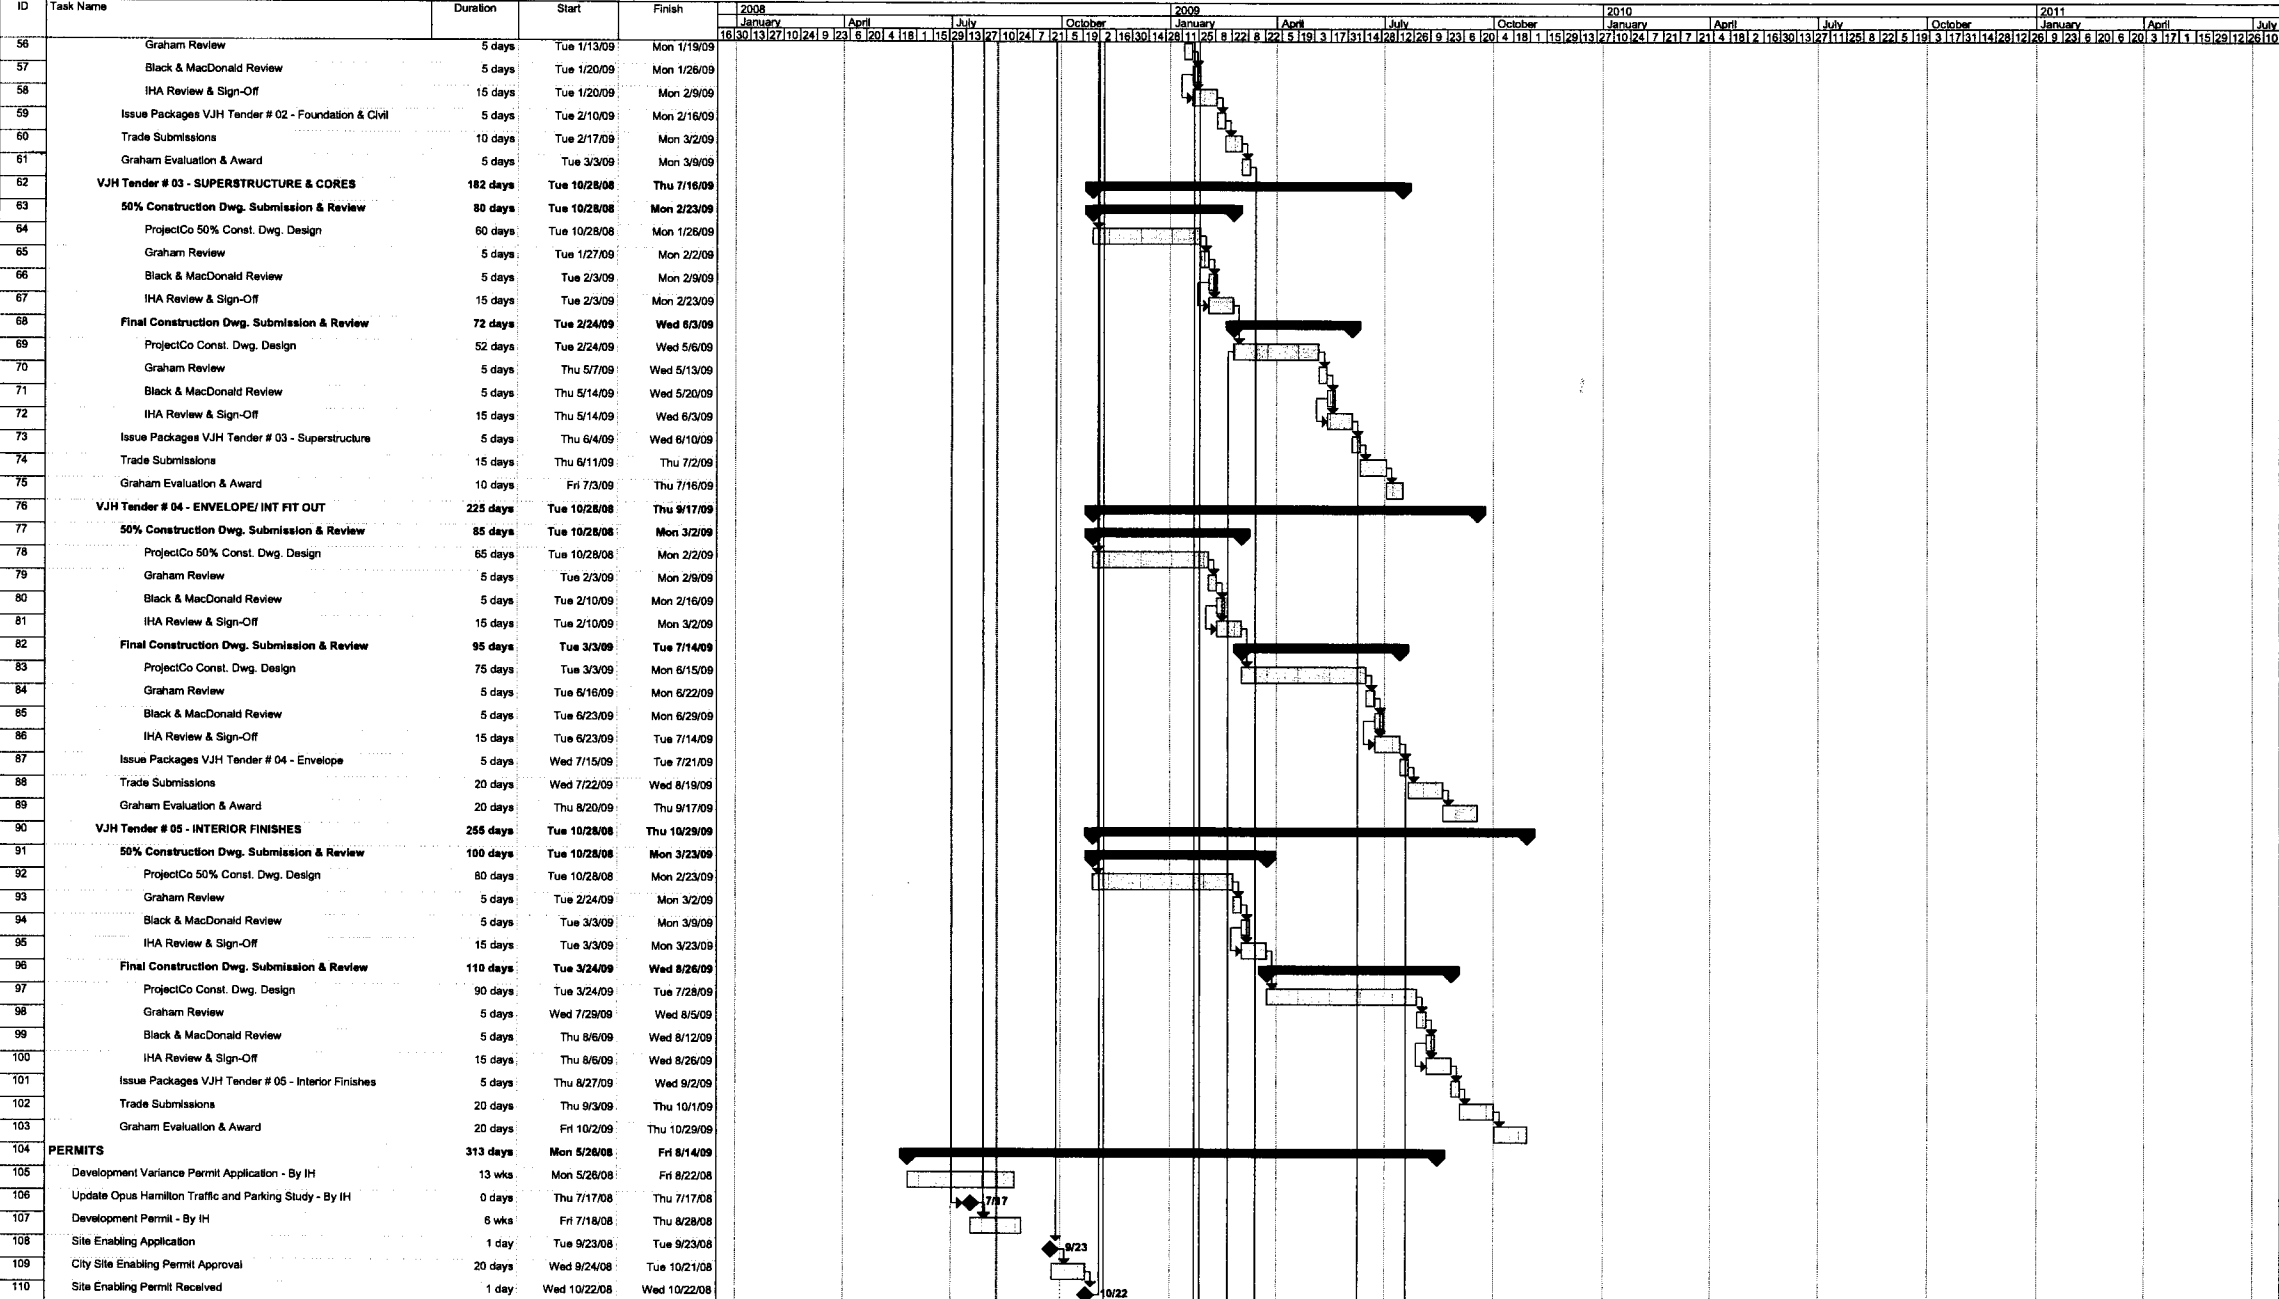


Project: VERNON - Summary Schedul Date: Fri 8/8/08

	Task		Progress		Summary		Rolled Up Critical Task		Rolled Up Progress		External Tasks		Group By Summary
	Critical Task		Milestone		Rolled Up Task		Rolled Up Milestone		Split		Project Summary		Deadline

VERNON JUBILEE HOSPITAL - DIAGNOSTIC AND TREATMENT BUILDING

Preliminary Schedule v.8 (with added floors) - Fri 8/8/08

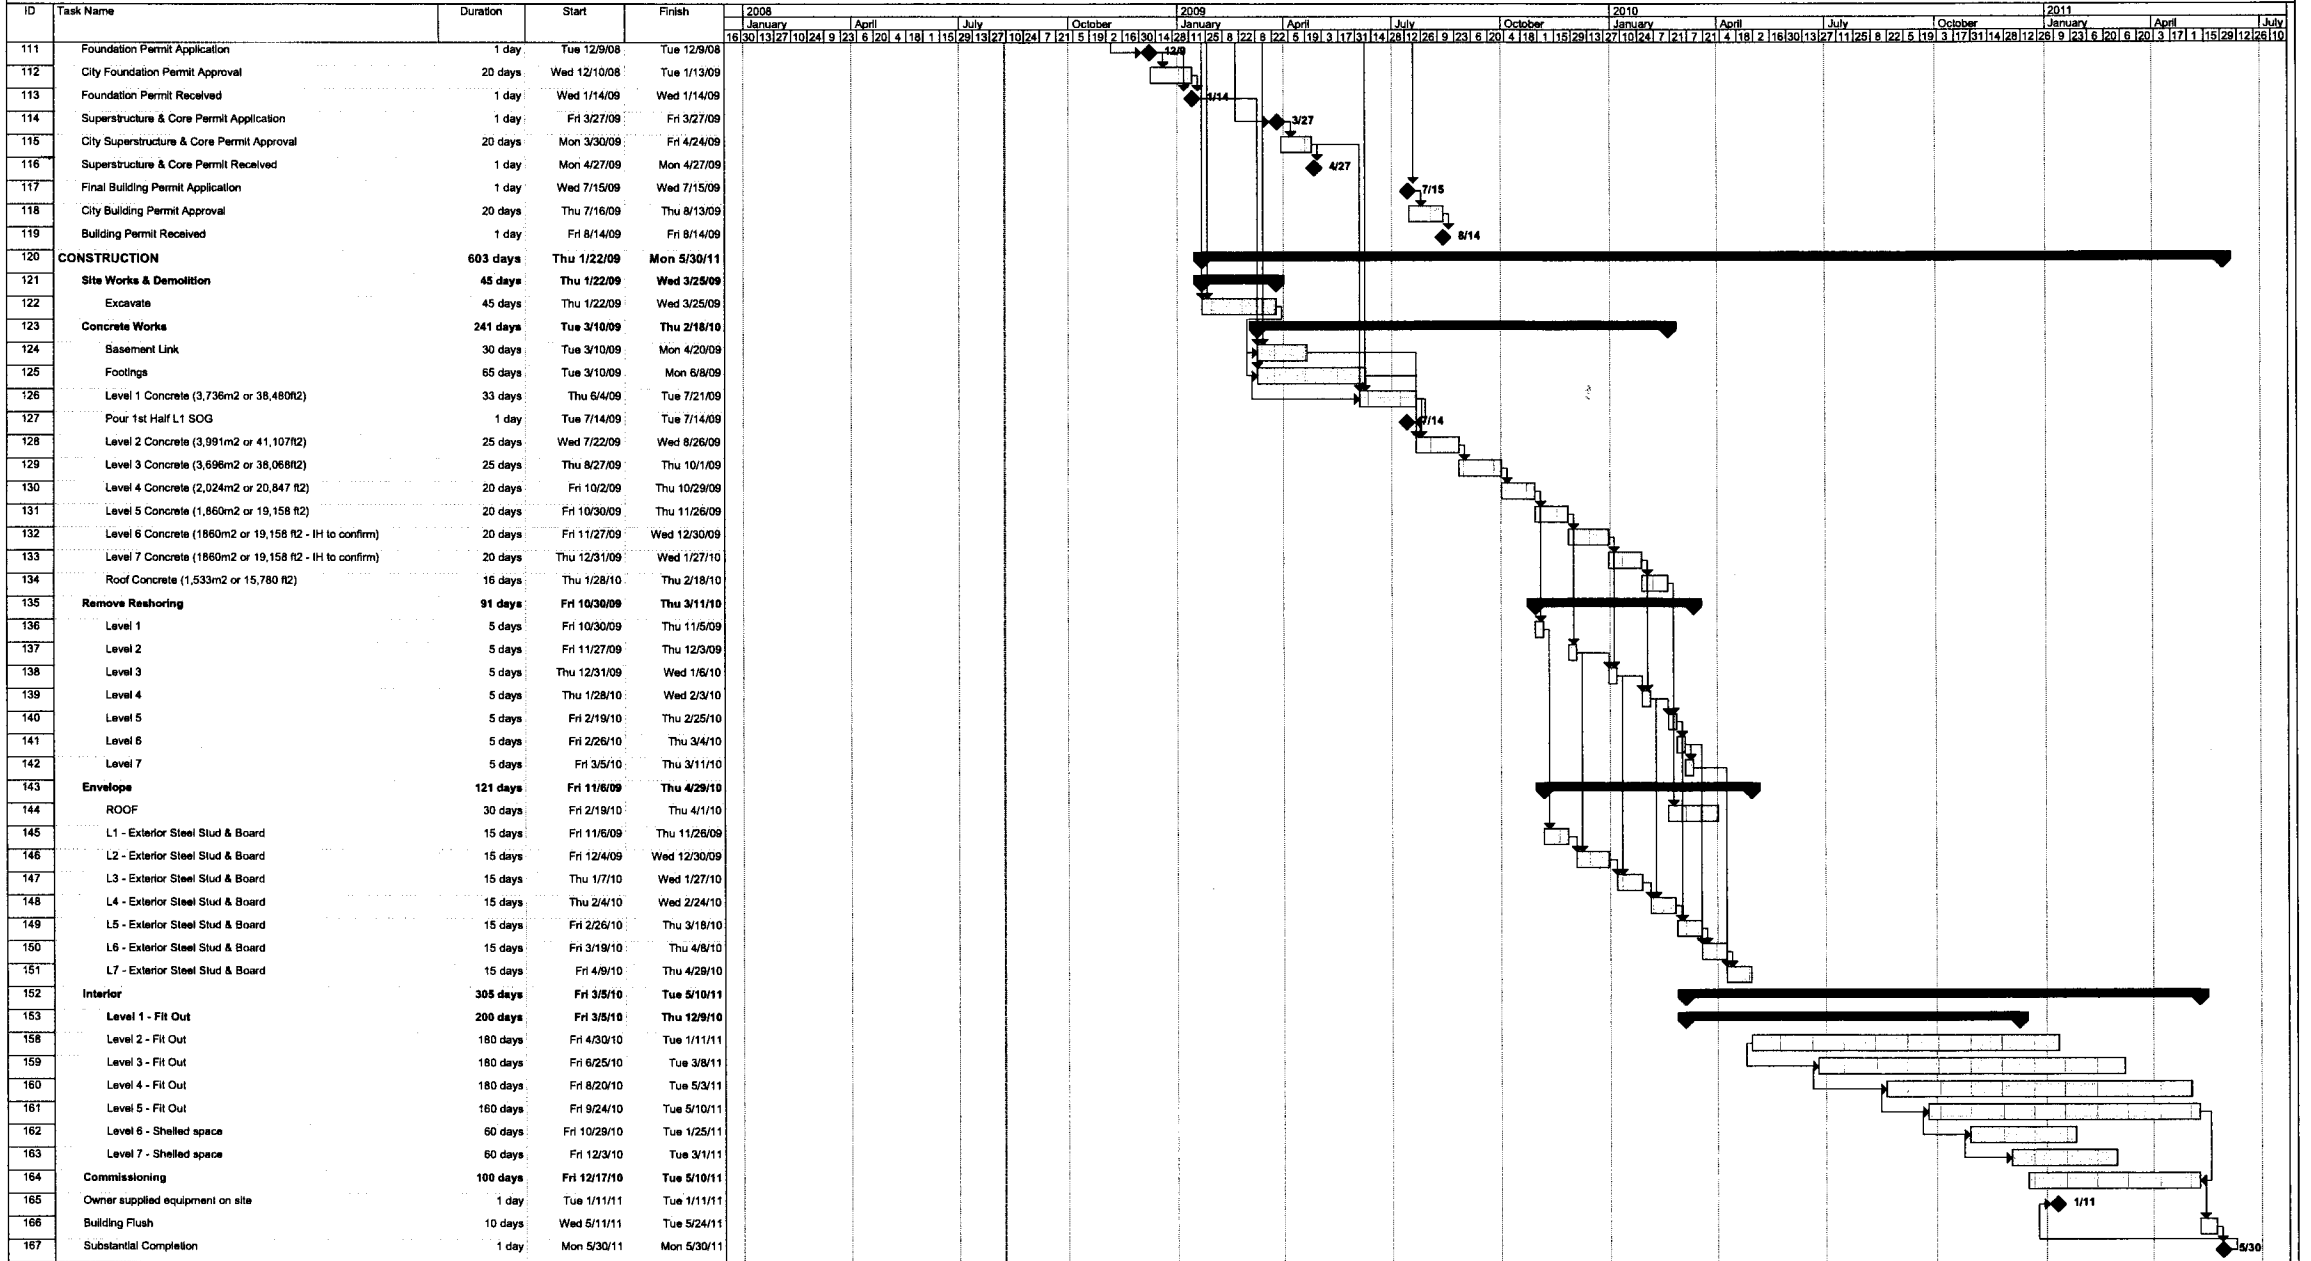

Project: VERNON - Summary Schedul Date: Fri 8/8/08

Task: [] Progress: [] Summary: [] Rolled Up Critical Task: [] Rolled Up Progress: [] External Tasks: [] Group By Summary: []

Critical Task: [] Milestone: [] Rolled Up Task: [] Rolled Up Milestone: [] Split: [] Project Summary: [] Deadline: []
